

9.6.2021


[Maria Joki-Pesola

Pohjoismaisen tasehallintahankkeen tilanne


Sähkömarkkinatoimikunta





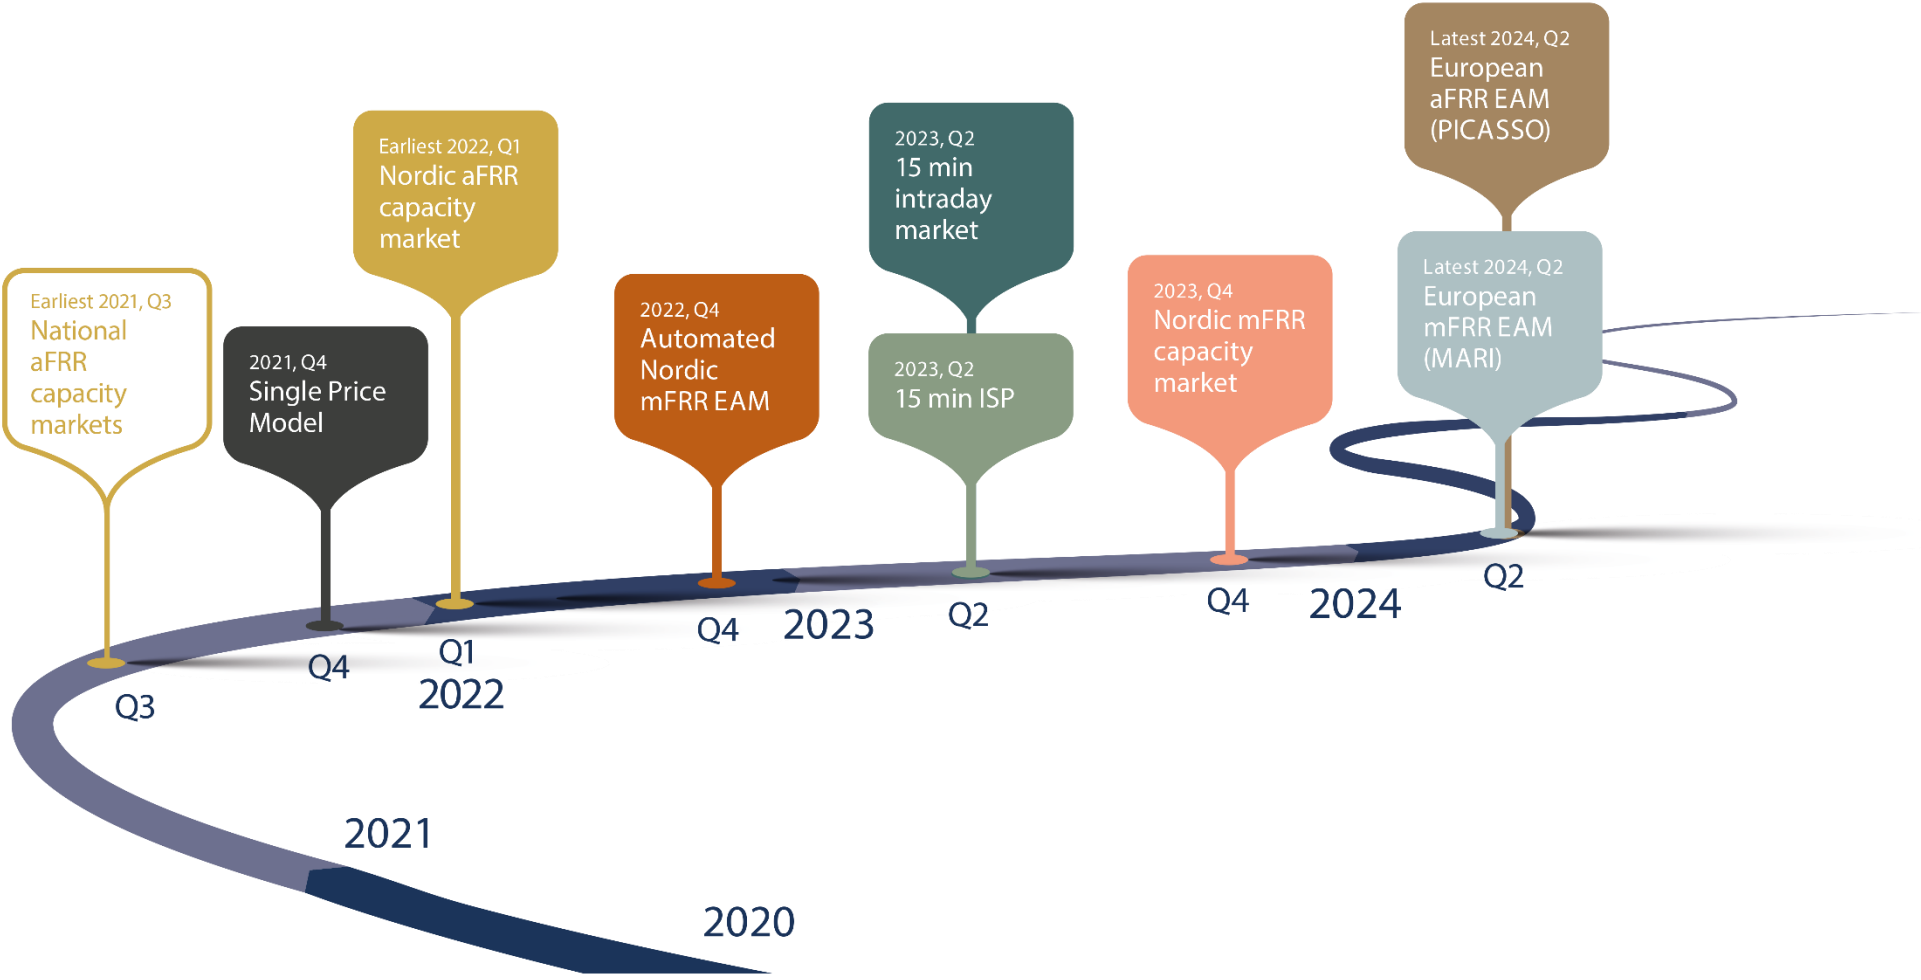



FINGRID

NBM roadmap



Overall status of the NBM program



Projects	Highlights Progress & Outlook	Current Status	Prognosis for Go-Live
Nordic mFRR EAM	Latest internal milestone delayed due to missing TSO data deliveries & quality. Inhibits planned real-life solution evaluation which is crucial for further development. Consequences and risks for subsequent milestones being assessed. Risk of delay on go-live date is high. Mitigating actions are first and foremost increased capacity and prioritization at each TSO.		
Nordic aFRR CM	Mostly on track for Nordic and local projects towards national and Nordic go-live. Some challenges inhibits final acceptance test progress and is driving risk for minor delays on test completion, especially driving risk of delay of national market go-live Statnett in Sept '21. External dependency on Nordic Flow-based does not influence progress on project deliveries – only the Nordic capacity go-live date targeted for Q1 '22.		
15 min ISP	Holistic monitoring structure under establishment to track all activities and deliveries required for 15 min ISP transition. Identification of required activities and deliveries is ongoing and a significant total scope is seen. TSOs derogation requests for May 22 nd '23 have been granted. Risk is currently driven primarily by the dependency on mFRR EAM go-live, hence the current prognosis for go-live.		
Single Price	Imbalance fee harmonization agreed for Fingrid, Statnett and Svenska Kraftnät. Energinet is investigating fee level nationally before joining the harmonized fee level. Minor progress challenges on technical deliveries due to dependency on ongoing Transparency Platform work but assessed as manageable.		
Nordic mFRR CM	Main project on hold as Nordic aFRR CM is prioritized first. On-going assessment of TSOs needs and priorities regarding both national and Nordic mFRR capacity markets to update execution plans. Possible resumption of the project summer '21.	N/A	
